



BROCKWAY
ENGINEERING
P.L.L.C.

Hydraulics

Hydrology

Water Resources

RECEIVED

JUL 06 2020

Department of Water Resources
Eastern Region

July 2, 2020

Regional Manager
Idaho Department of Water Resources
900 N. Skyline Drive, Suite A
Idaho Falls, ID 83402-1718

Re: Sam's Hollow Water Company – 2019 Annual Report
Project No. 370-04-2001

Dear Regional Manager:

Enclosed please find the 2019 annual report required by the approved mitigation plan for Sam's Hollow Water Company in Bear Lake. If you have any questions or need additional information, please do not hesitate to contact me.

Cordially,

Greg Sullivan, M.S., Engineer

Cc: Sam's Hollow Water Company
Enc: Sam's Hollow Water Company-3 Final Reports
Idaho Department of Water Resources Eastern Region-1 Final Report

CHARLES E.
BROCKWAY,
PH.D., P.E.

CHARLES G.
BROCKWAY,
PH.D., P.E.

2016 NORTH
WASHINGTON
STREET • SUITE 4

TWIN FALLS,
IDAHO 83301

208•736•8543

FAX: 736•8506

Project No. 370-01-1999

2019 Annual Report on Water Use and Mitigation for the Sam's Hollow Water Company

Prepared for:

**Sam's Hollow Water Company
Bear Lake, Idaho**

June 30, 2020

For information concerning this report, contact
Greg W. Sullivan, M.S., Engineer



CHARLES E. BROCKWAY, PH.D., P.E.
CHARLES G. BROCKWAY, PH.D., P.E.
ERICK POWELL, PH.D., P.E

2016 NORTH WASHINGTON, SUITE 4
TWIN FALLS, IDAHO 83301

Project No. 370-01-1999

2019 Annual Report on Water Use and Mitigation for the Sam's Hollow Water Company

Prepared for:

**Sam's Hollow Water Company
Bear Lake, Idaho**

June 30, 2020



For information concerning this report, contact
Greg W. Sullivan, M.S., Engineer



CHARLES E. BROCKWAY, PH.D., P.E.
CHARLES G. BROCKWAY, PH.D., P.E.
ERICK POWELL, PH.D., P.E.

2016 NORTH WASHINGTON, SUITE 4
TWIN FALLS, IDAHO 83301

2019 Annual Report on Water Use and Mitigation Sam's Hollow Water Company

Brockway Engineering, PLLC
June 30, 2020

Introduction

The Water Management and Operations Plan for Mitigation (the "Plan") dated June 19, 2006 for Sam's Hollow Water Company requires an annual report of water use on residences and facilities in use during the year. The Water Management and Operation Plan for Mitigation was amended February 10, 2015 by Rocky Mountain Environmental Associates Inc. The reporting requirements are outlined in the Plan, which was submitted to the Idaho Department of Water Resources. The Plan requires the submittal of the number and type of facilities (residences, commercial, and other) utilizing ground water during the year, the estimated depletion to Bear Lake resulting from the occupancy of the facilities, irrigated acres taken out of production within the project, and the volume of mitigation water returned to Bear Lake through the mitigation facilities.

The mitigation facilities consist of a water deliveries from the end of the irrigation system to Fish Haven Creek and a mitigation pipeline which conveys water to Bear Lake. The 2015 amended Plan changed the method of returning water to Bear Lake by including the option to discharging a portion of irrigation water back into Fish Haven Creek allowing it to flow down the creek into Bear Lake. Water is also delivered to Bear Lake through a mitigation pipeline that collects water at the end of the irrigation system. Water delivered through the irrigation system, the Fish Haven Creek bypass pipe and the mitigation pipeline is to be measured before mitigation water returns to Bear Lake.

Sam's Hollow Water Company has shares in Fish Haven Water Users for delivery through three ditches from Fish Haven Creek to the project. Deliveries into the ditches are measured through calibrated flumes. During 2019, deliveries through Ditch No. 3, the lower ditch, were the source of water for mitigation. A portion of the flow through

Ditch No. 3 was delivered into a pond and thence through the flow meter and into Bear Lake.

Project Build-Out History

In 2006 there were no homes or water-using facilities in use on the Project. Project build out varies from year to year but has steadily increased. In 2011, the Club House was constructed in the Project area. Table 1 provides the year and number of residences constructed in the Project, type of wastewater treatment and if construction occurred within the current place of use of irrigation water rights.

A total of six (6) houses were constructed in 2019. Of the six houses, five were constructed and connected to the Fish Haven Sewer District. One home was built that utilizes on-site wastewater treatment in 2019. The total number of residential households constructed in the project area is 76. Locations of the residences are shown on the attached map. A total of 16 residential homes and the clubhouse have been constructed inside of the irrigation place of use and qualify for mitigation acres.

Table 1: Residence Units Constructed Information

Residence Units Constructed					
Year	On-site Wastewater treatment	Fish Haven Sewer District	Condominium	Inside Irrigation Place of Use	Total Residences
2006					0
2007	1				1
2008		9		5	10
2009		4		1	14
2010		3		2	17
2011		6			23
2012	7	8		2	38
2013		2		1	40
2014		7		1	47
2015		2			49
2016	2	3			54
2017	2	8		1	64
2018	1	5		1	70
2019	1	5		2	76
Total	14	62	0	16	76

Irrigated Acres

Mitigation for water use on residential and commercial units requires that irrigated acres formerly supplied with surface water be dried up to compensate for consumptive use depletion of the development. The 2008 annual report documented the fact that 2.05 acres had been removed from irrigation due to construction of roadways (note that other roads were in place prior to the approved mitigation plan and are not accounted for). The assumed area of house footprints, driveways, and other hardscape areas per residence is 4,000 ft². The assumed area of turf, garden area and landscaping areas per residence is 5,000 ft² for a total displaced area of 9,000 ft² per residence. The approximate area removed from irrigation for the clubhouse, pool area and parking lot is 1.0 acres or 43,560 ft². Based on procedures developed by Dr. Robert Hill and adopted in the Bear River Ground Water Management Plan, the consumptive depletion for grass pasture is 1.18 ac-ft/acre/year.

Table 2 provides the total accumulated mitigation from the construction of structures within the water right place of use from the start of the project until the end of the current reporting year of 2019.

Table 2: Summary of Mitigation Provided by Construction through 2019.

		ft ² /structure	Acres	AFA
Road Ways			2.05	2.42
Homes	16	9000	3.31	3.90
Condos	0	12000	0.00	0.00
Commercial	1	43560	1.00	1.18

Total Removed for Mitigation 6.36 Acres 7.50 AFA

Estimated Project Depletion

The estimated consumptive depletion from residences and other facilities was determined using procedures developed by Dr. Robert Hill and adopted in the Bear River Ground Water Management Plan. For the Sam's Hollow system, the depletion values for potable water and irrigation of residences and commercial facilities were developed and included in the Plan for the project. Table 3 was developed to assist in estimating depletion each year based on the facilities build out. Table 3 shows the

annual unit depletion and the number of units on line in 2019. The total estimated depletion from the seventy six (76) units and club house on line in 2019 is 23.82 acre feet.

Table 3. Depletion analysis for Sam's Hollow Water Company in 2019. All depletions are in acre-feet annually.

Entities with On-Site Sewage Disposal

	Unit Depletion	Occupied Units	Total Depletion
Domestic Potable Water - Homesites	0.03	14	0.42
Irrigation - Homesites	0.14	14	1.96

Entities with St. Charles Sewer District Service

	Unit Depletion	Occupied Units	Total Depletion
Domestic Potable Water - Homesites	0.19	62	11.78
Irrigation - Homesites	0.14	62	8.68

Domestic/Irrigating - Condominiums (Per Building = 4 units)	0.5	0	0.00
Irrigation - Condominiums	0.14	0	0.00

Potable Water - Commercial	2.8	1	2.80
-----------------------------------	-----	---	------

All Depletion Values are in Acre-Feet Annually

The annual depletion value is based on a rate of 40.2% occupancy

Total Homesites	76
Total Condominiums	0
Total Commercial Sites	1
Total Depletion	25.64 afa

Water Supply Available for Mitigation

The 140.5 shares in Fish Haven Water Users owned by Sam's Hollow Water Company can be diverted through any of three ditches: the Upper North Ditch, Number 1 Ditch, and Number 3 Ditch. Each ditch has been instrumented with water measuring flumes and flow measurements have been recorded since May 22, 2004. The flumes were installed by the Fish Haven Water Users Company with assistance from Sam's Hollow Water Company and are being monitored by Sam's Hollow Water Company.

During 2019, discharge readings were obtained from June 4, 2019 through October 22, 2019 and are shown on the attached spreadsheet. This log shows that there was approximately 2,910.1 acre-feet of irrigation water diverted into Upper North Ramped Flume, Ditch No. 1 and Ditch No. 3 during the irrigation season of 2019, of which 551.6 acre-feet was allotted to Sam's Hollow Water Company. See Table 4.

Table 4. Discharge readings per month.

Month	Upper North acre feet	No 1 North acre feet	No. 3 North acre feet	Total acre feet
April	NA	NA	NA	NA
May	0.0	0.0	0.0	0.0
June	31.5	33.0	8.5	76.9
July	79.4	33.7	14.6	129.4
August	75.6	14.8	32.3	120.0
September	97.3	32.8	22.3	154.4
October	26.5	32.5	16.9	70.9
November	NA	NA	NA	NA
Total	310.3	146.7	94.6	551.6

As discussed in previous reports, 22.2 acres of previously irrigated land covered by the 140.5 shares in Fish Haven Water Users was dried up in 2009.

There have been 6.36 acres dried up due to construction of roads and buildings in the project irrigated area. The total irrigated acres that have been set aside to date for the project is 28.56 acres.

Mitigation Water Returned to Bear Lake

Water was returned to Bear Lake via the mitigation pipeline and was measured by the flow meter located just east of the Fish Haven Cemetery. The pipeline at the end of ditch 1, conveying water from the retention pond, under the highway, and to Bear Lake is an 8-inch PVC pipe with a Siemens SITRANS FM electromagnetic water meter Type MAG 8000 installed in the pipeline (see attached photograph). The meter has a totalizer and instantaneous discharge readout which reads in gallons and gallons per minute. The meter is maintained by Sam's Hollow staff.

The meter was installed in 2007 to record the mitigation water volume. For the 2019 season, mitigation flow commenced to Bear Lake on September 2, 2019. The mitigation flow turn terminated on November 14, 2019. Table 5 shows the mitigation pipeline flow meter readings. The volume returned to Bear Lake during the 2019 irrigation season through the mitigation pipelines was 20.99 acre feet.

Table 5. Flow Meter Readings for the Sam's Hollow Mitigation Pipeline.

Date	Reading (gallons)	Volume (acre-feet)
9/2/2019	38,970,500	119.60
11/4/2019	45,811,000	140.59

Mitigation Volume	6,840,500	20.99	acre-feet
-------------------	-----------	-------	-----------

In the amended mitigation plan that was finalized in 2015, the method of returning mitigation water to Bear Lake was modified. Instead of all of the water being delivered to Bear Lake through the meter that was installed in 2007, water will also be measured and delivered into Fish Haven Creek. This mitigation water is to be measured with a ramp flume installed on the end of the bypass pipe. Operation and measuring direction for the bypass pipe and flume designed by McMillen Engineering are included in the amended 2015 mitigation plan.

Water has been delivered annually into Fish Haven Creek since 2015 and is supplying mitigation for the Sam's Hollow Water Company. Table 6 shows the data for water diverted annually into Fish Haven Creek for 2019 that was collected from May 24, 2019 through November 7, 2019. The volume returned to Bear Lake through Fish Haven Creek diversions was 67.22 acre feet. The total volume of water returned to Bear Lake through the mitigation pipeline and the diversions into Fish Haven Creek during 2018 was 88.21 acre feet.

**Table 6. Flow Measurements for Fish Haven Creek Bypass
Ramped Flume into Fish Haven Creek.**

	Volume (acre-feet)
May	9.74
June	45.36
July	3.54
August	2.53
September	1.88
October	3.32
November	0.86
December	0.00

Total Mitigation Volume	<table border="1"><tr><td>67.22</td></tr></table>	67.22	acre-feet
67.22			

The consumptive use reduction appurtenant to the 6.36 acres removed from irrigation provided 7.50 acre feet to mitigate for the project depletion in 2019, which was insufficient to provide the entire mitigation requirement. Therefore, 15.37 acres (18.14 acre feet) of additional irrigated acres beyond those dried up on the residential footprints and roadways will be added to the mitigation acres for the current development build-out.

The additional 15.37 acres of additional irrigated acres to be dried up will come from the 22.2 acres that were dried up in 2009. The remaining total of 6.83 acres of the 22.2 acres is available for future mitigation needs.

At the conclusion of 2019, total recorded cumulative volume of water discharge into Bear Lake is 253.02 acre feet. The cumulative volume required for mitigation from project development is 182.55 acre feet (See Figure 1).

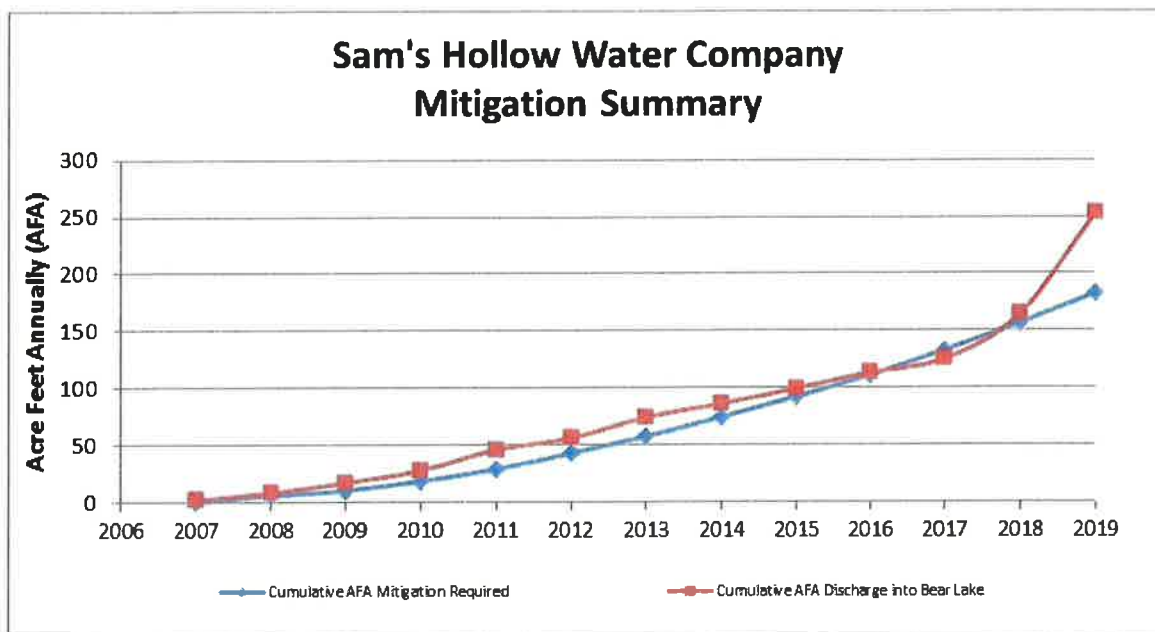


Figure 1: Sam's Hollow Water Company Mitigation Summary

Projection of 2020 Sufficiency of Mitigation Water

For 2020, based on a projected build-out, there will be 6 additional homes comprised of 5 residential homes outside of the irrigation area and 1 residential home within the water right place of use. Of the 6 additional homes, it is expected that there will be 1 additional residential homes with on-site sewage treatment. The total expected residential units online will be 82 units. The club house will continue to be utilized with no additional conversion of irrigated areas to commercial uses. The calculated depletion for residences and commercial uses under these assumptions will be 27.46 acre feet. It is estimated that the seasonal water availability for Sam's Hollow Water Company in 2020 will be adequate to provide mitigation water for the expected number of units on-line in 2020. Based on NRCS SNOTEL data for the Bear River Basin obtained on June 10, 2020, the peak snow water equivalent was 90% of the average level. The runoff for Fish Haven Creek will likely be considered average based on the snow pack data, and it is anticipated that water supply will be adequate for mitigation needs. Mitigation flow to Bear Lake from Ditch 1 will need to commence during late summer or early fall. Mitigation flow into Fish Haven Creek will continue to be measured and recorded so that it can be included in the total mitigation volume for the Sam's Hollow Water Company.

Regarding the consumptive use balance, the projected 82 units on line in 2020 (17 homes and the club house within the currently irrigated area) will provide a total of 6.77 acres or 7.99 acre-feet of the required 27.46 acre-feet estimated depletion for 2020. Therefore, 19.47 acre-feet must be provided from additional irrigation reduction in the amount of 16.50 acres. The 28.97 acres of previous irrigation retirement will be sufficient to mitigate for the proposed additional 2020 project depletion. There will be 5.70 acres of mitigation remaining from after the expected build out for 2020.



Terminus of the Sam's Hollow mitigation pipeline.

Note: Date on photo is incorrect. The correct date is July 2007.



Development that has occurred at Sam's Hollow Water Company as of 2018



Development that has occurred at Sam's Hollow Water Company as of 2018



Development that has occurred at Sam's Hollow Water Company as of 2018



Development that has occurred at Sam's Hollow Water Company as of 2018



Fish Haven Water Users Association

Date	Upper North Ramped Flume*						NO 1 NORTH " Parchal Flume"						No. 3 North 12" Ramped Flume						Total af/d	Sam's Hollow Total af/d
	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 99.5 shares 249.5 in ditch 39.9%	Accum af	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 20.0 shares 133.8 in ditch 15.0%	Accum af	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 21.0 shares 255.4 in ditch 8.2%	Accum af		
11-May																				
12-May																				
13-May																				
14-May																				
15-May																				
16-May																				
17-May																				
18-May																				
19-May																				
20-May																				
21-May																				
22-May																				
23-May																				
24-May																				
25-May																				
26-May																				
27-May																				
28-May																				
29-May																				
30-May																				
31-May																				
1-Jun																				
2-Jun																				
3-Jun																				
4-Jun	0	0.00	0.00	0.00	0.00	0.00	0	0.00	0.00	0.00	0.00	0.00	0.72	6.10	12.07	12.07	0.99	0.99	12.07	0.99
5-Jun				0.00	0.00	0.00				0.00	0.00	0.00				12.07	0.99	1.99	12.07	0.99
6-Jun	0	0.00	0.00	0.00	0.00	0.00	0	0.00	0.00	0.00	0.00	0.00	0.72	6.10	12.07	12.07	0.99	2.98	12.07	0.99
7-Jun				0.00	0.00	0.00				2.05	0.31	0.31				12.07	0.99	3.97	14.12	1.30
8-Jun				0.00	0.00	0.00				4.10	0.61	0.92				12.07	0.99	4.96	16.17	1.61
9-Jun				0.00	0.00	0.00				6.15	0.92	1.84				12.07	0.99	5.96	18.22	1.91
10-Jun				0.00	0.00	0.00				8.20	1.23	3.06				12.07	0.99	6.95	20.27	2.22
11-Jun	0	0.00	0.00	0.00	0.00	0.00	0.65	5.17	10.25	10.25	1.53	4.60	0.72	6.10	12.07	12.07	0.99	7.94	22.32	2.52
12-Jun				2.00	0.80	0.80				10.25	1.53	6.13				6.04	0.50	8.44	18.28	2.83
13-Jun	0.36	2.02	4.00	4.00	1.59	2.39	0.65	5.17	10.											

Date	Upper North Ramped Flume*						NO 1 NORTH " Parchal Flume"						No. 3 North 12" Ramped Flume						Sam's Hollow	
	Gage ft	Discharge cfs	Measured afd	Estimated afd	Sam's Hollow 99.5 shares 249.5 in ditch 39.9%	Accum af	Gage ft	Discharge cfs	Measured afd	Estimated afd	Sam's Hollow 20.0 shares 133.8 in ditch 15.0%	Accum af	Gage ft	Discharge cfs	Measured afd	Estimated afd	Sam's Hollow 21.0 shares 255.4 in ditch 8.2%	Accum af	Total afd	Total afd
14-Jul				5.70	2.27	67.37				7.62	1.14	51.84				5.36	0.44	11.43	18.68	3.85
15-Jul				5.50	2.19	69.56				7.62	1.14	52.98				6.49	0.53	11.96	19.60	3.87
16-Jul	0.43	2.68	5.30	5.30	2.11	71.67	0.54	3.85	7.62	7.62	1.14	54.12	0.54	3.85	7.62	7.62	0.63	12.59	20.53	3.88
17-Jul				5.30	2.11	73.79				7.62	1.14	55.25				7.62	0.63	13.22	20.53	3.88
18-Jul	0.43	2.68	5.30	5.30	2.11	75.90	0.54	3.85	7.62	7.62	1.14	56.39	0.54	3.85	7.62	7.62	0.63	13.84	20.53	3.88
19-Jul				5.50	2.19	78.09				7.62	1.14	57.53				7.62	0.63	14.47	20.73	3.96
20-Jul				5.70	2.27	80.37				7.62	1.14	58.67				7.62	0.63	15.09	20.93	4.04
21-Jul				5.91	2.35	82.72				7.62	1.14	59.81				7.62	0.63	15.72	21.14	4.12
22-Jul				6.11	2.44	85.16				7.62	1.14	60.95				7.62	0.63	16.35	21.34	4.20
23-Jul	0.48	3.19	6.31	6.31	2.52	87.67	0.54	3.85	7.62	7.62	1.14	62.09	0.54	3.85	7.62	7.62	0.63	16.97	21.54	4.28
24-Jul				6.31	2.52	90.19				7.62	1.14	63.23				7.62	0.63	17.60	21.54	4.28
25-Jul	0.48	3.19	6.31	6.31	2.52	92.71	0.54	3.85	7.62	7.62	1.14	64.36	0.54	3.85	7.62	7.62	0.63	18.22	21.54	4.28
26-Jul				7.25	2.89	95.60				6.09	0.91	65.27				9.07	0.75	18.97	22.41	4.55
27-Jul				8.19	3.27	98.87				4.57	0.68	65.96				10.52	0.86	19.84	23.28	4.82
28-Jul				9.13	3.64	102.51				3.05	0.46	66.41				11.97	0.98	20.82	24.15	5.08
29-Jul				10.07	4.02	106.53				1.52	0.23	66.64				13.42	1.10	21.92	25.02	5.35
30-Jul	0.68	5.56	11.01	11.01	4.39	110.92	0	0.00	0.00	0.00	0.00	66.64	0.82	7.51	14.88	14.88	1.22	23.15	25.89	5.62
31-Jul				11.01	4.39	115.31				0.00	0.00	66.64				14.88	1.22	24.37	25.89	5.62
1-Aug	0.68	5.56	11.01	11.01	4.39	119.70	0	0.00	0.00	0.00	0.00	66.64	0.82	7.51	14.88	14.88	1.22	25.59	25.89	5.62
2-Aug				11.01	4.39	124.10				0.00	0.00	66.64				14.88	1.22	26.82	25.89	5.62
3-Aug				11.01	4.39	128.49				0.00	0.00	66.64				14.88	1.22	28.04	25.89	5.62
4-Aug				11.01	4.39	132.88				0.00	0.00	66.64				14.88	1.22	29.26	25.89	5.62
5-Aug				11.01	4.39	137.27				0.00	0.00	66.64				14.88	1.22	30.49	25.89	5.62
6-Aug	0.68	5.56	11.01	11.01	4.39	141.66	0	0.00	0.00	0.00	0.00	66.64	0.82	7.51	14.88	14.88	1.22	31.71	25.89	5.62
7-Aug				11.01	4.39	146.06				0.00	0.00	66.64				14.88	1.22	32.93	25.89	5.62
8-Aug	0.68	5.56	11.01	11.01	4.39	150.45	0	0.00	0.00	0.00	0.00	66.64	0.82	7.51	14.88	14.88	1.22	34.15	25.89	5.62
9-Aug				10.07	4.02	154.47				0.00	0.00	66.64				14.88	1.22	35.38	24.95	5.24
10-Aug				9.13	3.64	158.11				0.00	0.00	66.64				14.88	1.22	36.60	24.01	4.87
11-Aug				8.19	3.27	161.38				0.00	0.00	66.64				14.88	1.22	37.82	23.07	4.49
12-Aug				7.25	2.89	164.27				0.00	0.00	66.64				14.88	1.22	39.05	22.13	4.11
13-Aug	0.48	3.19	6.31	6.31	2.52	166.78	0	0.00	0.00	0.00	0.00	66.64	0.82	7.51	14.88	14.88	1.22	40.27	21.19	3.74
14-Aug				6.31	2.52	169.30				0.00	0.00	66.64				13.75	1.13	41.40	20.06	3.65
15-Aug	0.48	3.19	6.31	6.31	2.52	171.82	0	0.00	0.00	0.00	0.00	66.64	0.74	6.37	12.61	12.61	1.04	42.44	18.93	3.55
16-Aug				6.31	2.52	174.33				1.52	0.23	66.87				12.61	1.04	43.47	20.45	3.78
17-Aug				6.31	2.52	176.85				3.05	0.46	67.32				12.61	1.04	44.51	21.97	4.01
18-Aug				6.31	2.52	179.37				4.57	0.68	68.01				12.61	1.04	45.55	23.49	4.24
19-Aug				6.31	2.52	181.88				6.09	0.91	68.92				12.61	1.04	46.59	25.02	4.46
20-Aug	0.48	3.19	6.31	6.31	2.52	184.40	0.54	3.85	7.62	7.62	1.14	70.06	0.74	6.37	12.61	12.61	1.04	47.62	26.54	4.69
21-Aug				3.16	1.26	185.66				7.62	1.14	71.20				12.61	1.04	48.66	23.39	3.43
22-Aug	0	0.00	0.00	0.00	0.00	185.66	0.54	3.85	7.62	7.62	1.14	72.34	0.74	6.37	12.61	12.61	1.04	49.70	20.23	2.18
23-Aug				0.00	0.00	185.66				7.62	1.14	73.47				12.61	1.04	50.73	20.23	2.18
24-Aug				0.00	0.00	185.66				7.62	1.14	74.61				12.61	1.04	51.77	20.23	2.18
25-Aug				0.00	0.00	185.66				7.62	1.14	75.75				12.61	1.04	52.81	20.23	2.18
26-Aug				0.00	0.00	185.66				7.62	1.14	76.89				12.61	1.04	53.85	20.23	2.18
27-Aug	0	0.00	0.00	0.00	0.00	185.66	0.54	3.85	7.62	7.62	1.14	78.03	0.74	6.37	12.61	12.61	1.04	54.88	20.23	2.18
28-Aug				0.00	0.00	185.66				7.62	1.14	79.17				6.31	0.52	55.40	13.92	1.66
29-Aug	0	0.00	0.00	0.00	0.00	185.66	0.54	3.85	7.62	7.62	1.14	80.31	0	0.00	0.00	0.00	0.00	55.40	7.62	1.14
30-Aug				2.20	0.88	186.54				7.62	1.14	81.45				0.00	0.00	55.40	9.82	2.02
31-Aug				4.41	1.76	188.30				7.62	1.14	82.58				0.00	0.00	55.40	12.02	2.90
1-Sep				6.61	2.64	190.93				7.62	1.14	83.72				0.00	0.00	55.40	14.22	3.77
2-Sep				8.81	3.51	194.44				7.62	1.14	84.86				0.00	0.00	55.40	16.43	4.65
3-Sep	0.68	5.56	11.01	11.01	4.39	198.84	0.54	3.85	7.62	7.62	1.14	86.00	0	0.00	0.00	0.00	0.00	55.40	18.63	5.53
4-Sep				11.01	4.39	203.23				6.76	1.01	87.01				0.00	0.00	55.40	17.77	5.40
5-Sep	0.68	5.56	11.01	11.01	4.39	207.62	0.46	2.98	5.90	5.90	0.88	87.89	0	0.00	0.00	0.00	0.00	55.40	16.91	5.27
6-Sep				11.01	4.39	212.01				5.90	0.88	88.77				0.00	0.00	55.40	16.91	5.27
7-Sep				11.01	4.39	216.41				5.90	0.88	89.66				0.00	0.00	55.40	16.91	5.27
8-Sep				11.01	4.39	220.80				5.90	0.88	90.54				0.00	0.00	55.40	16.91	5.27
9-Sep				11.01	4.39	225.19				5.90	0.88	91.42				0.00	0.00	55.40	16.91	5.27
10-Sep	0.68	5.56	11.01	11.01	4.39	229.58	0.46	2.98	5.90	5.90	0.88	92.30	0	0.00	0.00	0.00	0.00	55.40	16.91	5.27
11-Sep				11.01	4.39	233.98				5.90	0.88	93.18				0.00	0.00	55.40	16.91	5.27
12-Sep	0.68	5.56	11.01	11.01	4.39	238.37	0.46	2.98	5.90	5.90	0.88	94.06	0	0.00	0.00	0.00	0.00	55.40	16.91	5.27
13-Sep				10.07	4.02	242.39				5.90	0.88	94.95				0.00	0.00	55.40	15.97	4.90
14-Sep				9.13	3.64	246.03				5.90	0.88	95.83				0.00	0.00	55.40	15.03	4.52
15-Sep				8.19	3.27	249.29				5.90	0.88	96.71				0.00	0.00	55.40	14.09	4.15
16-Sep				7.25	2.89	252.19				5.90	0.88	97.59				0.00	0.00	55.40	13.15	3.77
17-Sep	0.48	3.19	6.31	6.31	2.52	254.70	0.46	2.98	5.90	5.90	0.88	98.47	0	0.00	0.00	0.00	0.00	55.40	12.21	3.40
18-Sep				6.31	2.52	257.22				5.90	0.88	99.36				13.01	1.07	56.47	25.21	4.47
19-Sep	0.48	3.19	6.31	6.31	2.52	259.74	0.46	2.98	5.90	5.90	0.88	100.24	1.16	13.14	26.01	26.01	2.14	58.61	38.22	5.54
20-Sep				6.31	2.52	262.25				6.77	1.01	101.25				26.01	2.14	60.75	39.09	5.67

Date	Upper North Ramped Flume*						NO 1 NORTH " Parchal Flume"						No. 3 North 12" Ramped Flume						Total af/d	Sam's Hollow Total af/d									
	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 99.5 shares 249.5 in ditch 39.9%	Accum af	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 20.0 shares 133.8 in ditch 15.0%	Accum af	Gage ft	Discharge cfs	Measured af/d	Estimated af/d	Sam's Hollow 21.0 shares 255.4 in ditch 8.2%	Accum af											
21-Sep	0.48	3.19	6.31	6.31	2.52	264.77	0.65	5.17	10.25	7.64	1.14	102.39	1.16	13.14	26.01	26.01	2.14	62.89	39.96	5.80									
22-Sep				6.31	2.52	267.29				8.51	1.27	103.66				26.01	2.14	65.03	40.83	5.93									
23-Sep				6.31	2.52	269.80				9.38	1.40	105.07				26.01	2.14	67.16	41.70	6.06									
24-Sep				6.31	2.52	272.32				10.25	1.53	106.60				26.01	2.14	69.30	42.57	6.19									
25-Sep	0.48	3.19	6.31	6.31	2.52	274.84	0.65	5.17	10.25	10.25	1.53	108.13	0.98	10.01	19.82	22.92	1.88	71.19	39.47	5.93									
26-Sep				6.31	2.52	277.35				10.25	1.53	109.66				19.82	1.63	72.82	36.38	5.68									
27-Sep				5.85	2.33	279.69				10.25	1.53	111.19				19.82	1.63	74.45	35.91	5.49									
28-Sep				5.38	2.15	281.83				10.25	1.53	112.73				19.82	1.63	76.08	35.45	5.31									
29-Sep	0.36	2.02	4.00	4.92	1.96	283.80	0.65	5.17	10.25	10.25	1.53	114.26	0.98	10.01	19.82	19.82	1.63	77.71	34.99	5.12									
30-Sep				4.46	1.78	285.57				10.25	1.53	115.79				19.82	1.63	79.34	34.52	4.94									
1-Oct				4.00	1.59	287.17				10.25	1.53	117.32				19.82	1.63	80.96	34.06	4.76									
2-Oct				4.00	1.59	288.76				8.93	1.34	118.66				13.72	1.13	82.09	26.64	4.06									
3-Oct	0.36	2.02	4.00	4.00	1.59	290.35	0.54	3.85	7.62	7.62	1.14	119.80	0.54	3.85	7.62	7.62	0.63	82.72	19.23	3.36									
4-Oct				4.00	1.59	291.95				7.62	1.14	120.93				7.62	0.63	83.34	19.23	3.36									
5-Oct				4.00	1.59	293.54				7.62	1.14	122.07				7.62	0.63	83.97	19.23	3.36									
6-Oct				4.00	1.59	295.13				7.62	1.14	123.21				7.62	0.63	84.60	19.23	3.36									
7-Oct	0.36	2.02	4.00	4.00	1.59	296.73	0.54	3.85	7.62	7.62	1.14	124.35	0.54	3.85	7.62	7.62	0.63	85.22	19.23	3.36									
8-Oct				4.00	1.59	298.32				7.62	1.14	125.49				7.62	0.63	85.85	19.23	3.36									
9-Oct				4.00	1.59	299.92				8.93	1.34	126.82				7.62	0.63	86.48	20.54	3.56									
10-Oct				4.00	1.59	301.51				10.25	1.53	128.36				7.62	0.63	87.10	21.86	3.75									
11-Oct	0.36	2.02	4.00	4.00	1.59	303.10	0.65	5.17	10.25	10.25	1.53	129.89	0.54	3.85	7.62	7.62	0.63	87.73	21.86	3.75									
12-Oct				4.00	1.59	304.70				10.25	1.53	131.42				7.62	0.63	88.35	21.86	3.75									
13-Oct				4.00	1.59	306.29				10.25	1.53	132.95				7.62	0.63	88.98	21.86	3.75									
14-Oct				4.00	1.59	307.88				10.25	1.53	134.48				7.62	0.63	89.61	21.86	3.75									
15-Oct	0.36	2.02	4.00	4.00	1.59	309.48	0.65	5.17	10.25	10.25	1.53	136.02	0.54	3.85	7.62	7.62	0.63	90.23	21.86	3.75									
16-Oct				2.00	0.80	310.27				10.25	1.53	137.55				7.62	0.63	90.86	19.86	2.95									
17-Oct				0	0.00	0.00				0.00	0.00	310.27				0.65	5.17	10.25	10.25	1.53	139.08	0.54	3.85	7.62	7.62	0.63	91.48	17.86	2.16
18-Oct				0.00	0.00	0.00				0.00	0.00	310.27				10.25	1.53	140.61	7.62	0.63	92.11	17.86	2.16						
19-Oct	0	0.00	0.00	0.00	0.00	310.27	0.65	5.17	10.25	10.25	1.53	142.15	0.54	3.85	7.62	7.62	0.63	92.74	17.86	2.16									
20-Oct				0.00	0.00	310.27				10.25	1.53	143.68				7.62	0.63	93.36	17.86	2.16									
21-Oct				0.00	0.00	310.27				10.25	1.53	145.21				7.62	0.63	93.99	17.86	2.16									
22-Oct				0.00	0.00	310.27				10.25	1.53	146.74				7.62	0.63	94.62	17.86	2.16									
23-Oct	0	0.00	0.00	0.00	0.00	310.27	0.65	5.17	10.25	0.00	0.00	146.74	0.54	3.85	7.62	0.00	0.00	94.62	0.00	0.00									
24-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
25-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
26-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
27-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
28-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
29-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
30-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
31-Oct				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
1-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
2-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
3-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
4-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
5-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
6-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
7-Nov				0.00	0.00	310.27				0.00	0.00	146.74				0.00	0.00	94.62	0.00	0.00									
8-Nov	0.00	0.00	310.27	0.00	0.00	146.74	0.00	0.00	94.62	0.00	0.00																		
9-Nov	0.00	0.00	310.27	0.00	0.00	146.74	0.00	0.00	94.62	0.00	0.00																		
10-Nov	0.00	0.00	310.27	0.00	0.00	146.74	0.00	0.00	94.62	0.00	0.00																		
May Total				0.00	0.00					0.00	0.00					0.00	0.00	0.00	0.00										
June Total				79.04	31.52					220.54	32.98					103.80	8.53		420.87	76.89									
July Total				199.10	79.40					225.13	33.66					177.73	14.61		610.35	129.43									
August Total				189.62	75.62					99.00	14.80					392.32	32.26		667.07	119.96									
Sept Total				243.88	97.26					219.43	32.81					271.28	22.30		757.09	154.42									
Oct. Total				66.39	26.48					217.24	32.48					205.67	16.91		454.77	70.93									
Annual Total				778.02	310.27					981.33	146.74					1150.79	94.62		2910.1	551.6 afa									

SAM'S HALLOW WATER COMPANY MITIGATION

Water Year 2019

Fish Haven Creek Bypass Ramped Flume

Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet
1/1/2019			2/11/2019			3/24/2019			5/4/2019			6/14/2019	41.8	46.92
1/2/2019			2/12/2019			3/25/2019			5/5/2019			6/15/2019	30.0	48.12
1/3/2019			2/13/2019			3/26/2019			5/6/2019			6/16/2019	27.5	49.13
1/4/2019			2/14/2019			3/27/2019			5/7/2019			6/17/2019	23.0	49.97
1/5/2019			2/15/2019			3/28/2019			5/8/2019			6/18/2019	20.6	50.68
1/6/2019			2/16/2019			3/29/2019			5/9/2019			6/19/2019	18.3	51.28
1/7/2019			2/17/2019			3/30/2019			5/10/2019			6/20/2019	15.6	51.83
1/8/2019			2/18/2019			3/31/2019			5/11/2019			6/21/2019	15.3	52.33
1/9/2019			2/19/2019			4/1/2019			5/12/2019			6/22/2019	13.1	52.77
1/10/2019			2/20/2019			4/2/2019			5/13/2019			6/23/2019	8.8	53.14
1/11/2019			2/21/2019			4/3/2019			5/14/2019			6/24/2019	8.2	53.41
1/12/2019			2/22/2019			4/4/2019			5/15/2019			6/25/2019	10.4	53.70
1/13/2019			2/23/2019			4/5/2019			5/16/2019			6/26/2019	9.2	54.03
1/14/2019			2/24/2019			4/6/2019			5/17/2019			6/27/2019	8.2	54.33
1/15/2019			2/25/2019			4/7/2019			5/18/2019			6/28/2019	8.2	54.59
1/16/2019			2/26/2019			4/8/2019			5/19/2019			6/29/2019	8.2	54.84
1/17/2019			2/27/2019			4/9/2019			5/20/2019			6/30/2019	7.5	55.09
1/18/2019			2/28/2019			4/10/2019			5/21/2019			7/1/2019	7.1	55.32
1/19/2019			3/1/2019			4/11/2019			5/22/2019			7/2/2019	7.2	55.55
1/20/2019			3/2/2019			4/12/2019			5/23/2019			7/3/2019	6.9	55.78
1/21/2019			3/3/2019			4/13/2019			5/24/2019	32.6	0.16	7/4/2019	8.3	56.02
1/22/2019			3/4/2019			4/14/2019			5/25/2019	25.1	1.05	7/5/2019	7.1	56.27
1/23/2019			3/5/2019			4/15/2019			5/26/2019	29.3	1.92	7/6/2019	6.9	56.50
1/24/2019			3/6/2019			4/16/2019			5/27/2019	41.1	3.06	7/7/2019	6.4	56.72
1/25/2019			3/7/2019			4/17/2019			5/28/2019	48.8	4.39	7/8/2019	6.4	56.93
1/26/2019			3/8/2019			4/18/2019			5/29/2019	53.4	5.89	7/9/2019	6.0	57.14
1/27/2019			3/9/2019			4/19/2019			5/30/2019	52.6	7.65	7/10/2019	5.9	57.34
1/28/2019			3/10/2019			4/20/2019			5/31/2019	66.6	9.73	7/11/2019	4.1	57.50
1/29/2019			3/11/2019			4/21/2019			6/1/2019	97.3	12.22	7/12/2019	4.1	57.63
1/30/2019			3/12/2019			4/22/2019			6/2/2019	89.4	15.08	7/13/2019	3.1	57.74
1/31/2019			3/13/2019			4/23/2019			6/3/2019	93.7	18.13	7/14/2019	2.5	57.84
2/1/2019			3/14/2019			4/24/2019			6/4/2019	101.0	21.34	7/15/2019	2.2	57.91
2/2/2019			3/15/2019			4/25/2019			6/5/2019	89.4	24.55	7/16/2019	2.1	57.99
2/3/2019			3/16/2019			4/26/2019			6/6/2019	99.2	27.78	7/17/2019	2.0	58.05
2/4/2019			3/17/2019			4/27/2019			6/7/2019	102.9	31.16	7/18/2019	1.9	58.12
2/5/2019			3/18/2019			4/28/2019			6/8/2019	106.4	34.59	7/19/2019	1.7	58.18
2/6/2019			3/19/2019			4/29/2019			6/9/2019	71.4	37.55	7/20/2019	0.7	58.24
2/7/2019			3/20/2019			4/30/2019			6/10/2019	76.0	39.89	7/21/2019	0.7	58.26
2/8/2019			3/21/2019			5/1/2019			6/11/2019	54.8	42.11	7/22/2019	1.2	58.28
2/9/2019			3/22/2019			5/2/2019			6/12/2019	49.8	43.95	7/23/2019	1.1	58.32
2/10/2019			3/23/2019			5/3/2019			6/13/2019	47.1	45.58	7/24/2019	1.0	58.36

SAM'S HALLOW WATER COMPANY MITIGATION

Water Year 2019

Fish Haven Creek Bypass Ramped Flume

Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet	Date	Dailey CFS	Accumulated Acre-Feet
7/25/2019	1.1	58.40	9/4/2019	0.6	61.23	10/15/2019	2.9	64.61	11/25/2019		
7/26/2019	1.1	58.43	9/5/2019	0.6	61.25	10/16/2019	2.9	64.70	11/26/2019		
7/27/2019	1.1	58.47	9/6/2019	1.7	61.29	10/17/2019	3.0	64.79	11/27/2019		
7/28/2019	1.0	58.52	9/7/2019	1.7	61.36	10/18/2019	2.9	64.89	11/28/2019		
7/29/2019	1.0	58.55	9/8/2019	2.2	61.42	10/19/2019	3.0	64.98	11/29/2019		
7/30/2019	1.0	58.58	9/9/2019	1.8	61.49	10/20/2019	2.9	65.08	11/30/2019		
7/31/2019	1.8	58.62	9/10/2019	2.1	61.55	10/21/2019	2.9	65.18	12/1/2019		
8/1/2019	1.0	58.67	9/11/2019	2.1	61.63	10/22/2019	2.9	65.27	12/2/2019		
8/2/2019	1.0	58.70	9/12/2019	1.9	61.70	10/23/2019	2.8	65.37	12/3/2019		
8/3/2019	2.1	58.77	9/13/2019	2.0	61.77	10/24/2019	2.8	65.47	12/4/2019		
8/4/2019	2.4	58.85	9/14/2019	1.8	61.83	10/25/2019	3.0	65.57	12/5/2019		
8/5/2019	2.3	58.93	9/15/2019	2.0	61.89	10/26/2019	2.8	65.67	12/6/2019		
8/6/2019	2.3	59.01	9/16/2019	1.8	61.96	10/27/2019	3.8	65.78	12/7/2019		
8/7/2019	2.4	59.10	9/17/2019	2.0	62.02	10/28/2019	4.3	65.91	12/8/2019		
8/8/2019	2.4	59.18	9/18/2019	1.9	62.08	10/29/2019	4.2	66.05	12/9/2019		
8/9/2019	2.2	59.25	9/19/2019	1.8	62.15	10/30/2019	4.5	66.22	12/10/2019		
8/10/2019	3.1	59.35	9/20/2019	1.9	62.21	10/31/2019	4.4	66.36	12/11/2019		
8/11/2019	3.1	59.45	9/21/2019	2.4	62.29	11/1/2019	4.2	66.49	12/12/2019		
8/12/2019	3.1	59.55	9/22/2019	2.3	62.36	11/2/2019	4.0	66.62	12/13/2019		
8/13/2019	2.5	59.65	9/23/2019	2.5	62.44	11/3/2019	3.9	66.75	12/14/2019		
8/14/2019	2.5	59.73	9/24/2019	2.4	62.51	11/4/2019	3.7	66.88	12/15/2019		
8/15/2019	3.9	59.83	9/25/2019	2.2	62.59	11/5/2019	4.1	67.00	12/16/2019		
8/16/2019	4.0	59.96	9/26/2019	2.2	62.66	11/6/2019	3.8	67.13	12/17/2019		
8/17/2019	4.0	60.09	9/27/2019	2.2	62.73	11/7/2019			12/18/2019		
8/18/2019	3.5	60.22	9/28/2019	3.1	62.82	11/8/2019			12/19/2019		
8/19/2019	3.5	60.33	9/29/2019	3.3	62.93	11/9/2019			12/20/2019		
8/20/2019	3.6	60.45	9/30/2019	3.2	63.03	11/10/2019			12/21/2019		
8/21/2019	3.4	60.57	10/1/2019	3.2	63.14	11/11/2019			12/22/2019		
8/22/2019	3.8	60.68	10/2/2019	3.1	63.24	11/12/2019			12/23/2019		
8/23/2019	2.2	60.80	10/3/2019	3.1	63.34	11/13/2019			12/24/2019		
8/24/2019	2.1	60.86	10/4/2019	3.1	63.44	11/14/2019			12/25/2019		
8/25/2019	2.0	60.93	10/5/2019	3.0	63.54	11/15/2019			12/26/2019		
8/26/2019	2.3	61.01	10/6/2019	3.0	63.63	11/16/2019			12/27/2019		
8/27/2019	0.9	61.06	10/7/2019	3.0	63.73	11/17/2019			12/28/2019		
8/28/2019	0.8	61.09	10/8/2019	2.9	63.83	11/18/2019			12/29/2019		
8/29/2019	0.7	61.12	10/9/2019	3.1	63.93	11/19/2019			12/30/2019		
8/30/2019	0.5	61.14	10/10/2019	4.7	64.07	11/20/2019			12/31/2019		
8/31/2019	0.5	61.16	10/11/2019	3.0	64.20	11/21/2019					
9/1/2019	0.6	61.17	10/12/2019	2.9	64.31	11/22/2019					
9/2/2019	0.6	61.19	10/13/2019	3.1	64.42	11/23/2019					
9/3/2019	0.5	61.21	10/14/2019	2.8	64.51	11/24/2019					
