GENERAL PUMP MECHANICS, INC.

14815 N EDENCREST DRIVE
SPOKANE, WA 99208
(509) 465-8658

Invoice

DATE	INVOICE #
6/29/2007	133000

*NOTE: ALL INFORMATION IS TRUE AND CORRECT — AND ON 06/29/07 (LISTED ABOVE) IS WHEN THE WELL WENT ON LINE.

R. TALMO
03/02/2010

$10.00 CATALOG

BILL TO

TALMO,BRENT
3411 ALTURA AVE.
LACRESCENTA,CA.91214

TERMS	DUE DATE	PROJECT
Due on receipt	6/29/2007	

ITEM	DESCRIPTION	QTY	RATE	AMOUNT
PUMP	GOULDS 2 HP. 5 GPM. SUBMERSIABLE PUMP	1	1,290.00	1,290.00T
CONTROL BOX	2 HP. FRANKLIN CONTROL BOX	1	150.00	150.00T
PIPE	GALVENIZED 11/4"	693	2.49	1,725.57T
WIRE	#8/4 SUB- CONDUCTOR	703	2.47	1,736.41T
CHECK VALVE	CHECK VALVE 11/4"	3	39.00	117.00T
CAP	6" WELL CAP	1	59.50	59.50T
PITLESS	DICKENS PITLESS ADAPTER	1	90.00	90.00T
ELECT. HDWR,	ELECTRICAL FITTINGS	1	95.00	95.00T
PERMIT	ELECTRICAL PERMIT	1	60.00	60.00T
H20 ANALYSIS	BACTERIA AND NITRATE ANALYSIS	1	60.00	60.00T
HYDRANT	FROST FREE HYDRANT & MISC. GALVINIZED FITTINGS	1	149.00	149.00T
PUMP SAVER	PUMP SAVER 233 AMPERAGE MONITOR	1	250.00	250.00T
FORD CONNECTO	11/4" FORD BRONZE CONNECTOR WITH INSERT	1	49.50	49.50T
FLOW TEST	4 HOUR FLOW TEST	1	150.00	150.00T
LABOR	PUMP RIG INSTALLATION LABOR	1	510.00	510.00T
	BRENT,WENT OVER THE ESTIMATE,DO TO HYDRANT,PUMP SAVER & FITTINGS. ANY QUESTIONS PLEASE CALL ME. ITS BEEN A PLEASURE,THANK YOU !!!!!!!!!!!!!			
	6 % MATERIALS ONLY		6.00%	389.52

SAND HYDRANT WAS FROST — MOTOR IS CHEAPER THAN S.S.

THANK YOU FOLKS, WE APPRECIATE THE WORK!!

Total $6,881.50

296.00

XEROX CATALOGS WITH FLOW TEST

SCANNED
MAR - 5 2010

Form 238-7
6/02

IDAHO DEPARTMENT OF WATER RESOURCES
WELL DRILLER'S REPORT

Office Use Only
Well ID No.
Inspected by
Twp ____ Rge ____ Sec ____
____ 1/4 ____ 1/4 ____ 1/4
Lat: : : Long: : :

1. **WELL TAG NO.** D 0041195
DRILLING PERMIT NO. 837986
Water Right or Injection Well No.

2. **OWNER:**
Name Brent Talmo
Address 3411 Altura Ave.
City La Crescenta State Ca. Zip 91214

3. **LOCATION OF WELL by legal description:**
You must provide address or Lot, Blk, Sub. or Directions to well.
Twp. 4N North ☒ or South ☐
Rge. 2W East ☐ or West ☒
Sec. 9, ____ 1/4 (10 acres) S/E 1/4 (40 acres) N/E 1/4 (160 acres)
Gov't Lot ____ County Benewah
Lat: : : Long: : :
Address of Well Site Cassandra Hills Rd. 2 mi Left 1/4 mi Right Side City St. Maries
(Give at least name of road + Distance to Road or Landmark)
Lt. ____ Blk. ____ Sub. Name ____

4. **USE:**
☒ Domestic ☐ Municipal ☐ Monitor ☐ Irrigation
☐ Thermal ☐ Injection ☐ Other ____

5. **TYPE OF WORK** check all that apply (Replacement etc.)
☒ New Well ☐ Modify ☐ Abandonment ☐ Other ____

6. **DRILL METHOD:**
☒ Air Rotary ☐ Cable ☐ Mud Rotary ☐ Other ____

7. **SEALING PROCEDURES**

Seal Material	From	To	Weight / Volume	Seal Placement Method
Bentonite	0	30	10sx	Pour Around Pipe

Was drive shoe used? ☒ Y ☐ N Shoe Depth(s) 99
Was drive shoe seal tested? ☒ Y ☐ N How? Air

8. **CASING/LINER:**

Diameter	From	To	Gauge	Material	Casing	Liner	Welded	Threaded
6"	+1	-99	250	Steel	☒	☐	☒	☐
4"	-12	-722	160	PVC	☐	☒	☐	☐
					☐	☐	☐	☐

Length of Headpipe ____ Length of Tailpipe ____
Packer ☐ Y ☒ N Type ____

9. **PERFORATIONS/SCREENS PACKER TYPE**
Perforation Method Drill
Screen Type & Method of Installation ____

From	To	Slot Size	Number	Diameter	Material	Casing	Liner
642	702	3/4"	45	4"	PVC	☐	☒
140	460	3/4	8	4"	PVC	☐	☒
						☐	☐

10. **FILTER PACK**

Filter Material	From	To	Weight / Volume	Placement Method
none				

11. **STATIC WATER LEVEL OR ARTESIAN PRESSURE:**
205 ft. below ground Artesian pressure ____ lb.
Depth flow encountered 680 ft. Describe access port or control devices: ____
well Cap
46N 2W 9

12. **WELL TESTS:**
☐ Pump ☐ Bailer ☒ Air ☐ Flowing Artesian

Yield gal./min.	Drawdown	Pumping Level	Time
10gpm	Air lift	from	722

Water Temp. 40° Bottom hole temp. ____
Water Quality test or comments: Clear no color
Depth first Water Encounter 450

13. **LITHOLOGIC LOG:** (Describe repairs or abandonment)

Bore Dia.	From	To	Remarks: Lithology, Water Quality & Temperature	Water Y	Water N
8"	0	86	Clay-Top w/Shale		
	86	99	Shale Gray		
6"	99	150	Shale Gray		
	150	151	Shale Gray w/water 1/2 gpm	✓	
	151	680	Shale Gray		
	680	700	Shale Gray w/water 10 gpm	✓	
	700	722	Shale Gray		

RECEIVED
MAR 08 2006
IDWR/NIGP

Completed Depth 722 (Measurable)
Date: Started 12-31-05 Completed 1-30-06

14. **DRILLER'S CERTIFICATION**
I/We certify that all minimum well construction standards were complied with at the time the rig was removed.

Company Name Action Drilling Firm No. 618
Principal Driller Alvin Carris Date 2-25-06
and
Driller or Operator II ____ Date ____
Operator I Alvin Carris Date 2-25-06
Principal Driller and Rig Operator *Required*.
Operator I must have signature of Driller/Operator II.

FORWARD WHITE COPY TO WATER RESOURCES

SCANNED
MAR - 5 2010

SCANNED
MAR - 5 2010

TALMO PIN RP46N02W091001A

*NOTE: NUMBERS BELOW ARE G.P.S COORDINATES.

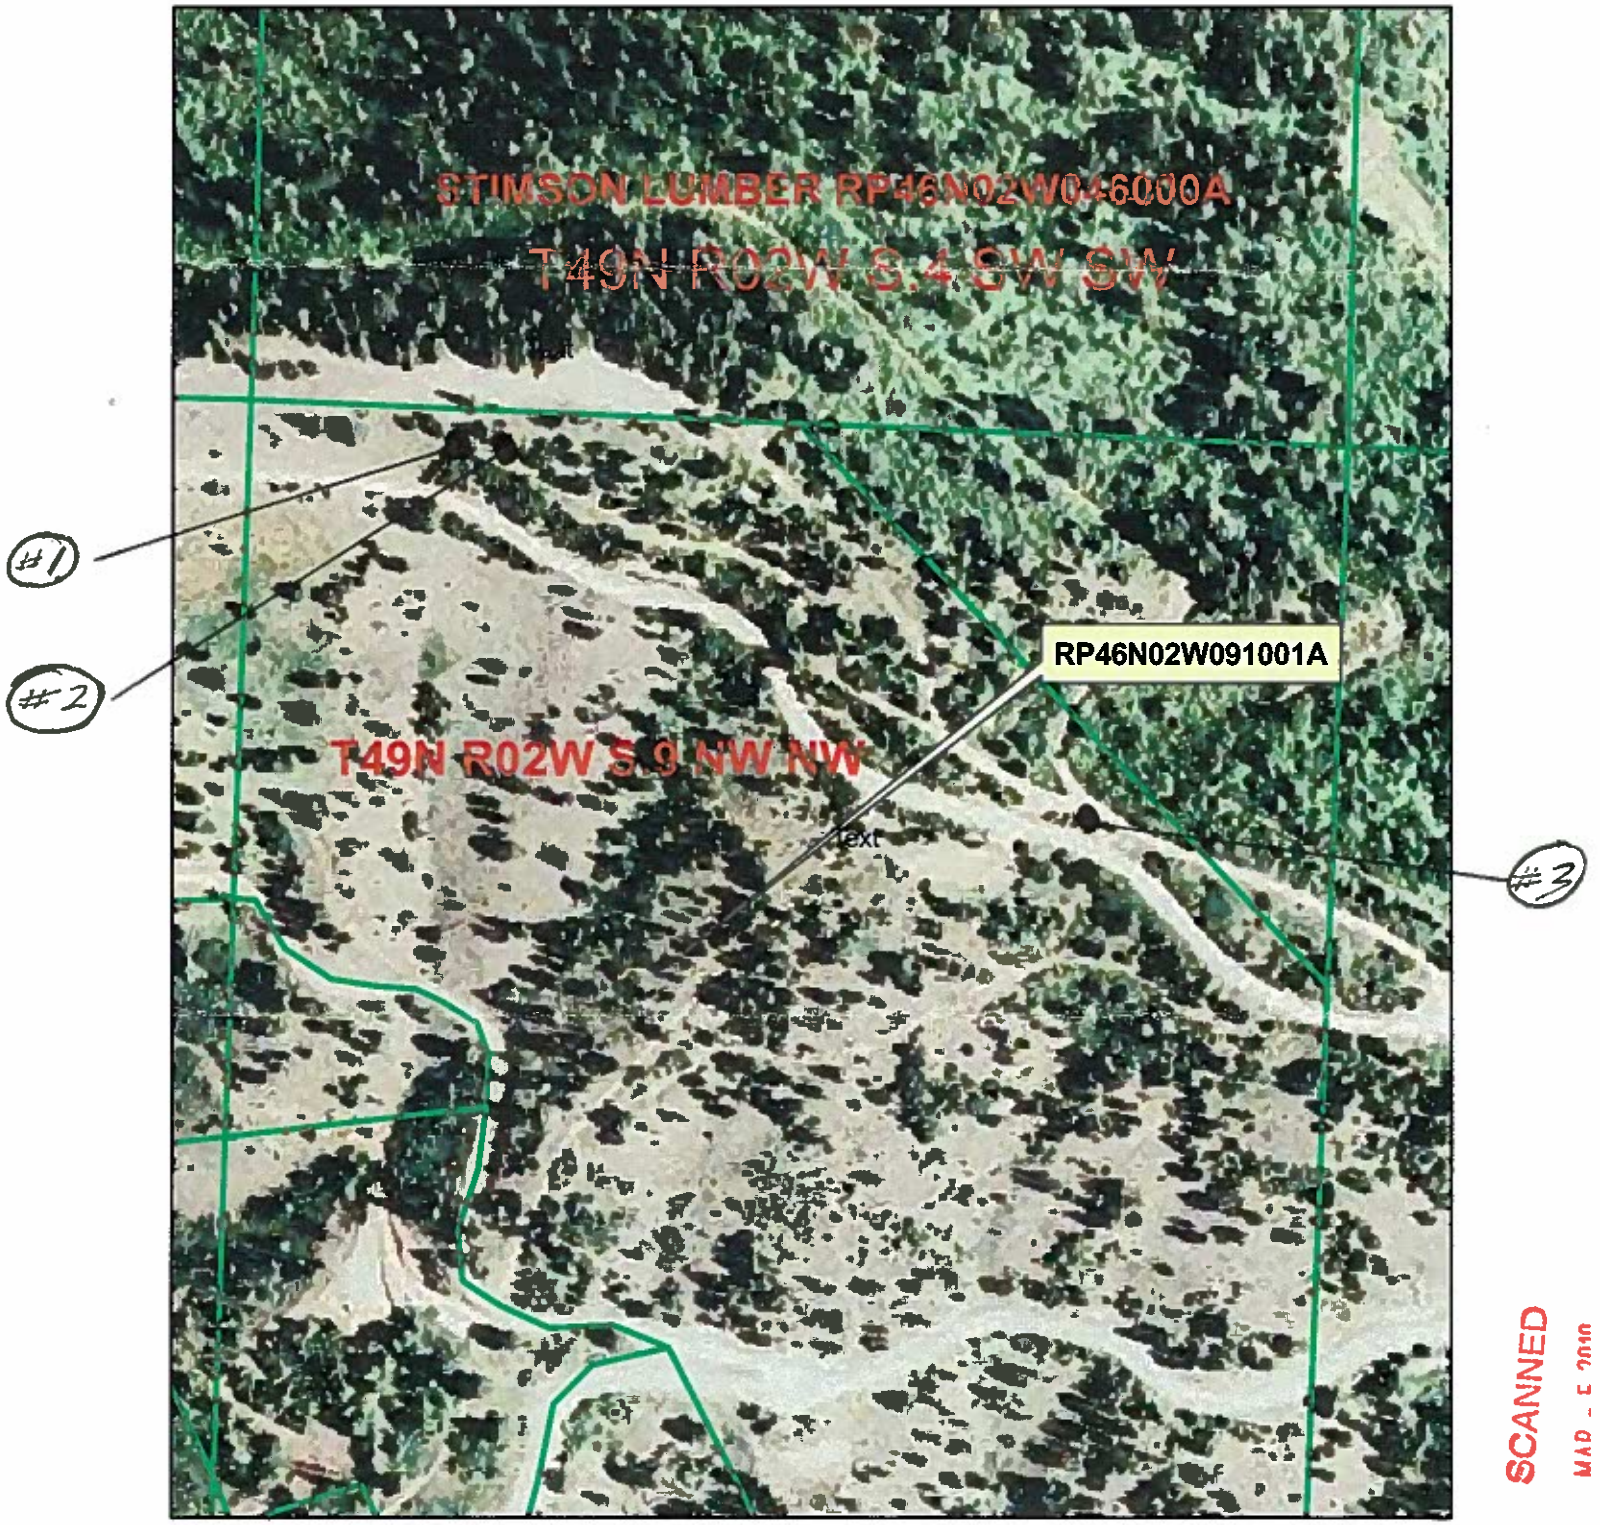

#1-HOUSE-N 47 DEGREES, 21.313 MINS. W 116 DEGREES, 36.386 MINS.
#2-CISTERN-N 47 DEGREES, 21.312 MINS. W 116 DEGREES, 36.334 MINS.
#3-WELL-N 47 DEGREES, 21.228 MINS. W 116 DEGREES, 36.194 MINS.

SCANNED
MAR - 5 2010
