Form 238-7
1/78

RECEIVED
JUN 4 1984
Department of Water Resources

STATE OF IDAHO
DEPARTMENT OF WATER RESOURCES

WELL DRILLER'S REPORT

State law requires that this report be filed with the Director, Department of Water Resources within 30 days after the completion or abandonment of the well.

USE TYPEWRITER OR BALLPOINT PEN

ENT'D

N

1. WELL OWNER

Name Jerry D. Allbee
P.O. Box 768
Address Newport, WA 99156

Owner's Permit No. 96-84-N-43

2. NATURE OF WORK

☒ New well ☐ Deepened ☐ Replacement
☐ Abandoned (describe method of abandoning) _____

3. PROPOSED USE

☒ Domestic ☐ Irrigation ☐ Test ☐ Municipal
☐ Industrial ☐ Stock ☐ Waste Disposal or Injection
☐ Other _____ (specify type)

4. METHOD DRILLED

☒ Rotary ☒ Air ☐ Hydraulic ☐ Reverse rotary
☐ Cable ☐ Dug ☐ Other _____

5. WELL CONSTRUCTION

Casing schedule: ☒ Steel ☐ Concrete ☐ Other _____

Thickness		Diameter		From		To	
.250	inches	6	inches +	1	feet	79	feet
	inches		inches		feet		feet
	inches		inches		feet		feet
	inches		inches		feet		feet

Was casing drive shoe used? ☒ Yes ☐ No
Was a packer or seal used? ☐ Yes ☒ No
Perforated? ☐ Yes ☒ No
How perforated? ☐ Factory ☐ Knife ☐ Torch
Size of perforation _____ inches by _____ inches

Number		From	To
_____	perforations	_____ feet	_____ feet
_____	perforations	_____ feet	_____ feet
_____	perforations	_____ feet	_____ feet

Well screen installed? ☐ Yes ☒ No
Manufacturer's name _____
Type _____ Model No. _____
Diameter ___ Slot size ___ Set from _____ feet to _____ feet
Diameter ___ Slot size ___ Set from _____ feet to _____ feet
Gravel packed? ☒ Yes ☐ No ☐ Size of gravel 1"
Placed from 75' feet to 79' feet
Surface seal depth 19 Material used in seal: ☐ Cement grout
bentoniteX ☐ Puddling clay
Sealing procedure used: ☐ Slurry pit ☐ Temp. surface casing
☒ Overbore to seal depth
Method of joining casing: ☐ Threaded ☒ Welded ☐ Solvent Weld
☐ Cemented between strata
Describe access port _____

7. WATER LEVEL

Static water level 56 feet below land surface.
Flowing? ☐ Yes ☒ No G.P.M. flow _____
Artesian closed-in pressure _____ p.s.i.
Controlled by: ☐ Valve ☐ Cap ☐ Plug
Temperature ____ °F. Quality _____

8. WELL TEST DATA

☐ Pump ☐ Bailer ☒ Air ☐ Other _____

Discharge G.P.M.	Pumping Level	Hours Pumped
13 GPM - ESTIMATED AIRLIFT		

9. LITHOLOGIC LOG

Hole Diam.	Depth From	Depth To	Material	Water Yes	Water No
6"	0	12	Sand, fine		X
6"	12	46	Sand & gravel, course		X
6"	46	60	Sand & gravel, course w/clay		X
6"	60	80	Sand & some gravel, course	X	
			NO PVC Liner Installed		
			6" Drive shoe Installed		

004286

RECEIVED
JUN 30 1984
Department of Water Resources
Northern District Office

MICROFILMED

10.

Work started 5/21/84 finished 5/21/84

6. LOCATION OF WELL

Sketch map location must agree with written location.

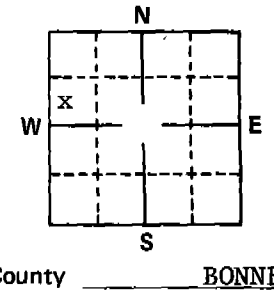

Subdivision Name _____
Lot No. _____ Block No. _____

County BONNER

SW ¼ NW ¼ Sec. 31, T. 56N N/S, R. 5W E/W.

11. DRILLERS CERTIFICATION

I/We certify that all minimum well construction standards were complied with at the time the rig was removed.

Firm Name PONDEROSA DRILLING Firm No. 228
E. 6010 Broadway
Address Spokane, WA 99212 Date 5/21/84

Signed by (Firm Official) W. Scott Barratt
and
(Operator) Lynnwood E. Hendrick

Lynnwood E. Hendrick

USE ADDITIONAL SHEETS IF NECESSARY — FORWARD THE WHITE COPY TO THE DEPARTMENT
